APPROVAL OF C.R.S.

S.No.	RECKONING THE ADEQUATE DISTANCE UNDER THE PROVISION OF G.R.3.40(1)(b)	APPROVAL NO.
1	FOR RECEPTION OF A DOWN TRAIN ON COMMON LOOP THE ADEQUATE DISTANCE IS RECKONED AS 144m FROM STARTER NO. 4 WHEN POINT NO.31 NORMAL SET TO BUFFER STOP.	SC/9/11-12 DT.12-07-2011
2	FOR RECEPTION OF AN UP TRAIN ON COMMON LOOP THE ADEQUATE DISTANCE IS RECKONED FROM STARTER NO. 44 WHEN POINT NO.24 NORMAL SET TO SAND HUMP.	
3	FOR RECEPTION OF A DN TRAIN ON GOODS R&D LINE No.1 OR GOODS R&D LINE No.2 THE ADEQUATE DISTANCE IS RECKONED AS 209m FROM STARTER NO. 5 OR 6 RESPECTIVELY WITH POINT NO.29 NORMAL SET TO BUFFER STOP.	
4	FOR RECEPTION OF A UP TRAIN ON GOODS R&D LINE No.1 OR GOODS R&D LINE No.2 THE ADEQUATE DISTANCE IS RECKONED AS 242m FROM STARTER NO. 46 OR 45 RESPECTIVELY SET TO OVERSHOOT LINE/SIDING WITH POINT NO. 21 NORMAL AND TRAP POINT No.22 NORMAL(OPEN).	
	NOTE FOR ALL OTHER RECEPTION MOVEMENTS THE ADEUATE DISTANCE SHALL BE RECKONED BEYOND TRAILING POINTS.	

DESCRIPTION OF FUNCTIONS

FUNCTION NO.	DESCRIPTION
1	DN HOME
1A	DN CALLING ON BELOW DN HOME
2	SPARE
3	DN STARTER – DN MAIN
4	DN STARTER – COMMON LOOP
5	DN STARTER – GOODS R&D LINE No.1
6	DN STARTER – GOODS R&D LINE No.2
7	SPARE
8	DN ADVANCED STARTER
9	GATE CONTROL – LC.145
10	SHUNT – UP MAIN – TO CLEAR OF SH36 OR SH37 OR SH38 OR SH39 OR SH40 OR SH44 OR SH48
11	SHUNT – TM. SIDING – TO CLEAR OF SH36 OR SH37 OR SH38
12	SHUNT – RTPP SIDING – TO CLEAR OF SH36 OR SH37
13	SHUNT – UP MAIN – TO CLEAR OF SH35
14	SHUNT – UP LOOP – TO CLEAR OF SH35
15	CONTROL FOR AUTOMATIC BLOCK WORKING–DN DIRECTION
16	CONTROL FOR AUTOMATIC BLOCK WORKING–UP DIRECTION
17	POINTS
18	POINTS
19	TRAP POINT
20	POINTS
21	POINTS
22	TRAP POINT
23	POINTS
24	POINTS
25	POINTS
26	SPARE
27	SPARE
28	POINTS
29	POINTS
30	POINTS

FUNCTION NO.	DESCRIPTION
31	POINTS
32	POINTS
33	POINTS
34	SPARE
35	SHUNT – DN MAIN– TO CLEAR OF SH13 OR SH14 OR S3 OR S4 S5 OR S6
36	SHUNT – GOODS R&D LINE No.2 – TO CLEAR OF SH10 OR SH11 OR SH12
37	SHUNT – GOODS R&D LINE No.1 – TO CLEAR OF SH10 OR SH11 OR SH12
38	SHUNT – UP LOOP – TO CLEAR OF SH10 OR SH11
39	SHUNT – DN MAIN TO CLEAR OF SH10
40	SHUNT – DEAD END SIDING TO CLEAR OF SH10
41	SPARE
42	SPARE
43	UP ADVANCED STARTER
44	UP STARTER – COMMON LOOP
45	UP STARTER – GOODS R&D LINE No.2
46	UP STARTER – GOODS R&D LINE No.1
47	UP STARTER – UP LOOP
48	UP STARTER – UP MAIN
49	SPARE
50	UP HOME
50A	UP CALLING ON UP HOME

(KMH–MOO' AUTOMATIC BLOCK SECTION TRACK SECTION TABLE

TRACK SECTION TABLE (DN LINE)

S.NO	TRACK SECTION	FROM	TO
1	A35DNAC	DA2	DA4
	B35DNAC	DB2	DB4
2	A3082AC	DA6	DA8
	B3028AC	DB6	DB8
3	A3102AC	DA10	DA12
	B3102AC	DB10	DB12
4	A3112AC	DA14	DA16
	B3112AC	DB14	DB16
5	A3122AC	DA18	DA20
	B3122AC	DB18	DB20

TRACK SECTION TABLE (UP LINE)

S.NO	TRACK SECTION	FROM	TO
1	A43UPAC	DA1	DA3
	B43UPAC	DB1	DB3
2	A3121AC	DA5	DA7
	B3121AC	DB5	DB7
3	A3101AC	DA9	DA11
	A3101AC	DB9	DB11
4	A3091AC	DA13	DA15
	B3091AC	DB13	DB15
5	A3081AC	DA17	DA19
	B3081AC	DB17	DB19

SUPERVISORY TRACK SECTION TABLE(DN LINE)

S.NO	TRACK SECTION	FROM	TO
1	SA35DNAC–3082AC	DA2	DA8
	SB35DNAC–3082AC	DB2	DB8
2	SA3082AC–3112AC	DA6	DA16
	SB3028AC–3112AC	DB6	DB16
3	SA3122AC–3122AC	DA14	DA20
	SB3122AC–3122AC	DB14	DB20
4	SA35DNAC–3122AC	DA2	DA20
	SB35DNAC–3122AC	DB2	DB20

SUPERVISORY TRACK SECTION TABLE(UP LINE)

S.NO	TRACK SECTION	FROM	TO
1	SA43UPAC–3121AC	DA1	DA7
	SB43UPAC–3121AC	DB1	DB7
2	SA3121AC–3091AC	DA5	DA15
	SB3121AC–3091AC	DB5	DB15
3	SA3091AC–3081AC	DA13	DA19
	SB3091AC–3081AC	DB13	DB19
4	SA43UPAC–3081AC	DA1	DA19
	SB43UPAC–3081AC	DB1	DB19

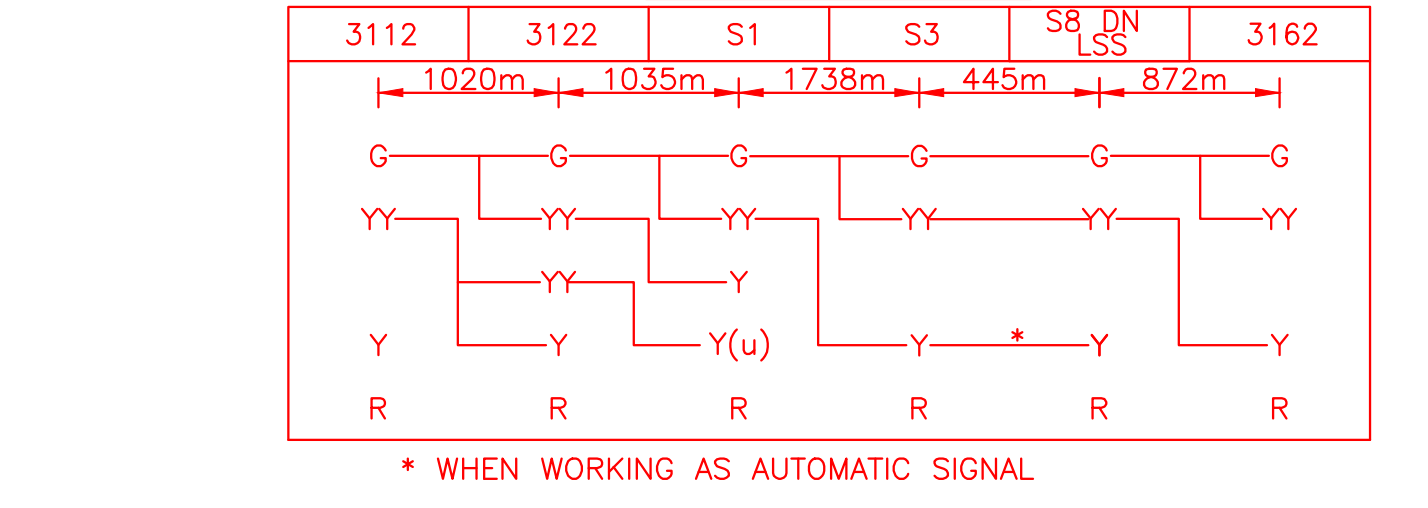
DOWN
ASPECT SEQUENCE CHART
3112
3122
S1
S3
S8 DN LSS
3162
1020m
1035m
1738m
445m
872m
G
YY
Y
Y(u)
R
*

* WHEN WORKING AS AUTOMATIC SIGNAL

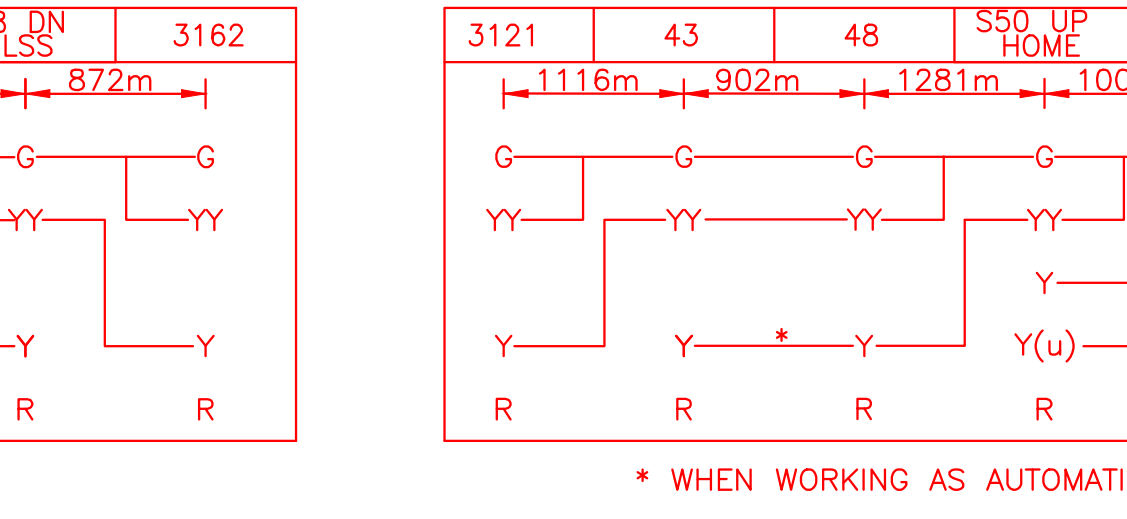
ASPECT SEQUENCE CHART
UP
3121
43
48
S50 UP HOME
3161
3171
1116m
902m
1281m
1004m
1015m
G
YY
Y
Y(u)
R
*

* WHEN WORKING AS AUTOMATIC SIGNAL

RENIGUNTA JN.(RU)
(KALAMALLA-8.25Km)(KMH)
GOOTY JN(GY)
(MANGAPATNAM-15.92Km)(MUM)
GP Km.310.940
GP Km.312.150
GP Km.313.350
GP CH.313518.00
PT 17B CH.313568.771m
PT 17A CH.313666.271m
PT 18B CH.313679.271m
PT 20B CH.313762.641m
PT 18A CH.313776.771m
GP CH.314070.00
PT 24B CH.314123.141m
PT 24A CH.314222.381m
PT 25B CH.314235.381m
PT 25A CH.314315.381m
GP CH.314493.52
BS CH.314715.381m
GP CH.314749.03
FOB CH.314996.11m
GP CH.315064.611
PT 31A CH.315151.531m
PT 31B CH.315249.031m
PT 32A CH.315262.031m
BS CH.315271.531m
PT 32B & 33A CH.315359.531m
PT 33B CH.315453.012m
GP CH.315503.110
Km.315.620
ARCH BRIDGE No.627
PSC BRIDGE No.627
DN MAIN
UP MAIN
NEUTRAL SECTION Km.312/18-20
NEUTRAL SECTION Km.312/19-17
@Km.310/11-09 ABS HUT
LINE VERIFICATION BOX 1A-AC 1-AC
LOCO PILOTS: DRAW AHEAD UPTO HOME SIGNAL IF HOME SIGNAL IS DANGER FOR CALLING ON SIGNAL
LINE VERIFICATION BOX 17B-AC 24-AC 25-AC 18-AC
LINE VERIFICATION BOX 43-AC 44-48-AC 17A-AC
LINE VERIFICATION BOX 20B-AC 20A-AC 21B-AC 21A-AC 23-AC
LINE VERIFICATION BOX 31A-AC 31B-AC 33B-AC 3-6-AC 8-AC
LINE VERIFICATION BOX 28-AC 30-AC 33A-AC 50-AC 50A-AC
TRACK MACHINE SIDING (200m)(CSR 200m)
TMS
TO RTPP SIDING LINE
RTPP
DEAD END SIDING (CSR: 400m)
H.L. PASSENGER PLATFORM (550m)
UP ← COMMON LOOP → DOWN
DOWN MAIN
← UP MAIN
← UP LOOP
UP ← GOODS R&D LINE No.1 → DOWN
UP ← GOODS R&D LINE No.2 → DOWN
(CSR 720m)
NOT FOR STABLING
EKT FOR CRANK HANDLE
CH1 POINTS 24.25.31
CH2 POINTS 17.18
CH3 POINTS 20.30
CH4 POINTS 19.21.29
CH5 POINTS 22.23.28
CH6 POINTS 32.33
LV(CO-OP) RESET BOX FOR AUTO SECTION
PREPARATORY RESET BOX FOR AUTO SECTION
DN LINE
UP LINE
STATION BUILDING
(EI-ROUTE SETTING) DUAL VDU CONTROL TERMINAL 1-50 FUNCTIONS
SPARE FUNCTION No.: 2.7.26.27.34.41.42.49.
WITH LC No.145
UP ⬌ DN
N
WITH SM
SLIDING BOOM LOCKING KEY 'OUT'
LIFTING BOOM KEY 'OUT'
SLIDING BOOM LOCKING KEY 'IN'
KEY FROM BOOM 'A' OUT
KEY FROM BOOM 'B' OUT
WINCH WITH KEY 'IN'
BOOM LOCKING KEY 'IN'
1-LEVER G.F. FOR BOOM LOCKING (UNLOCKED BY WINCH KEY)
WINCH KEY 'OUT'
PAD LOCK KEY OF BOOM 'A'
PAD LOCK KEY OF BOOM 'B'
'SPL' CLASS L.C.NO.145 AT Km.315/3-4(WTT) CH: 315379.951m GATE CONTROL:-9
588m FROM CL
BOOM'A'
BOOM'B'
KEY 'IN'
KEY 'OUT'
GIRDER BRIDGE No.635 4X10.5m Km: 315/525.49
BSLB
LOCO PILOTS: DRAW AHEAD UPTO HOME SIGNAL IF HOME SIGNAL IS DANGER FOR CALLING ON SIGNAL
3112-TS
43-TS
8-TS
3161-TS
3162-TS
3171-TS
1296m FROM CL
180m
120m
242m
635m
209m
230m
445m
144m
872m
1033m
1004m
1015m
3112
3122
3121
3161
3162
3171
3172

SYSTEM OF BLOCK WORKING

S.No.	SYSTEM	SECTION	BLOCK INSTRUMENT	TRACK DETECTION IN AUTOMATIC BLOCK SECTION BY	REMARKS,IF ANY
1	AUTOMATIC BLOCK	B–C SEC.	------	MSDAC	DUAL
2	AUTOMATIC BLOCK	A–B SEC.	------	MSDAC	DUAL

TRACK SECTIONS TABLE (DOWN LINE)

S.NO.	TRACK SECTION	FROM	TO
1	ABDNAC	DA2	DA4
	BBDNAC	DB2	DB4
2	A3162AC	DA6	DA8
	B3162AC	DB6	DB8
3	A3172AC	DA10	DA12
	B3172AC	DB10	DB12
4	A3182AC	DA14	DA16
	B3182AC	DB14	DB16
5	A3192AC	DA18	DA20
	B3192AC	DB18	DB20
6	A3202AC	DA22	DA24
	B3202AC	DB22	DB24
7	A3212AC	DA26	DA28
	B3212AC	DB26	DB28
8	A3222AC	DA30	DA32
	B3222AC	DB30	DB32
9	A3232AC	DA34	DA36
	B3232AC	DB34	DB36
10	A3242AC	DA38	DA40
	B3242AC	DB38	DB40
11	A3252AC	DA42	DA44
	B3252AC	DB42	DB44
12	A3262AC	DA46	DA48
	B3262AC	DB46	DB48
13	A3272AC	DA50	DA52
	B3272AC	DB50	DB52
14	A3282AC	DA54	DA56
	B3282AC	DB54	DB56

TRACK SECTIONS TABLE (UP LINE)

S.NO.	TRACK SECTION	FROM	TO
1	A25UPAC	DA1	DA3
	B25UPAC	DB1	DB3
2	A3291AC	DA5	DA7
	B3291AC	DB5	DB7
3	A3281AC	DA9	DA11
	B3281AC	DB9	DB11
4	A3271AC	DA13	DA15
	B3271AC	DB13	DB15
5	A3261AC	DA17	DA19
	B3261AC	DB17	DB19
6	A3241AC	DA21	DA23
	B3241AC	DB21	DB23
7	A3231AC	DA25	DA27
	B3231AC	DB25	DB27
8	A3221AC	DA29	DA31
	B3221AC	DB29	DB31
9	A3211AC	DA33	DA35
	B3211AC	DB33	DB35
10	A3201AC	DA37	DA39
	B3201AC	DB37	DB39
11	A3191AC	DA41	DA43
	B3191AC	DB41	DB43
12	A3181AC	DA45	DA47
	B3181AC	DB45	DB47
13	A3171AC	DA49	DA51
	B3171AC	DB49	DB51
14	A3161AC	DA53	DA55
	B3161AC	DB53	DB55

SUPERVISORY TRACK SECTIONS TABLE (DOWN LINE)

S.NO.	TRACK SECTION	FROM	TO
1	ABDNAC–A3162AC	DA2	DA8
	BBDNAC–B3162AC	DB2	DB8
2	A3162AC–A3182AC	DA6	DA16
	B3162AC–B3182AC	DB6	DB16
3	A3182AC–A3202AC	DA14	DA24
	B3182AC–B3202AC	DB14	DB24
4	A3202AC–A3222AC	DA22	DA32
	B3202AC–B3222AC	DB22	DB32
5	A3222AC–A3242AC	DA30	DA40
	B3222AC–B3242AC	DB30	DB40
6	A3242AC–A3262AC	DA38	DA48
	B3242AC–B3262AC	DB38	DB48
7	A3262AC–A3282AC	DA46	DA56
	B3262AC–B3282AC	DB46	DB56
8	ABDNAC–A3282AC	DA2	DA56
	BBDNAC–B3282AC	DB2	DB56

SUPERVISORY TRACK SECTIONS TABLE (UP LINE)

S.NO.	TRACK SECTION	FROM	TO
1	A25UPAC–A3291AC	DA1	DA7
	B25UPAC–B3291AC	DB1	DB7
2	A3291AC–A3271AC	DA5	DA15
	B3291AC–B3271AC	DB5	DB15
3	A3271AC–A3241AC	DA13	DA23
	B3271AC–B3241AC	DB13	DB23
4	A3241AC–A3221AC	DA21	DA31
	B3241AC–B3221AC	DB21	DB31
5	A3221AC–A3201AC	DA29	DA39
	B3221AC–B3201AC	DB29	DB39
6	A3201AC–A3181AC	DA37	DA47
	B3201AC–B3181AC	DB37	DB47
7	A3181AC–A3161AC	DA45	DA55
	B3181AC–B3161AC	DB45	DB55
8	A25UPAC–A3161AC	DA1	DA55
	B25UPAC–B3161AC	DB1	DB55

NOTES:–

1. THIS SIP WILL COME INTO FORCE ONLY ON COMPLETION OF THE WORK PROPOSED.
2. SYSTEM OF WORKING IS AUTOMATIC BLOCK SYSTEM.
3. TELE COMMUNICATION IS PROVIDED BETWEEN SM/MOO & LC.NO.145.
4. TRACK DETECTION IN AUTOMATIC SECTION BY DUAL MSDAC.
5. ☎ DENOTES APPROACH WARNING ARRANGEMENTS.
6. GRADIENTS FOR AUTOMATIC SECTION ARE SHOWN AS PER INDEX PLAN.
7. AUTOMATIC SIGNAL 3161 & 3162 ARE FED FROM MUDDANUR STATION.
8. THE FOLLOWING DPs IN AUTOMATIC BLOCK SECTION BETWEEN MOO–MUM ARE FED FROM MOO STATION
   - (A). UP LINE –DA51,DB51,DA53,DB53,DA55,DB55.
   - (B). DN LINE –DA2,DB2,DA4,DB4,DA6,DB6.
9. THE FOLLOWING DPs IN AUTOMATIC BLOCK SECTION BETWEEN MOO–KMH ARE FED FROM MOO STATION
   - (A). UP LINE –DA1,DB1
   - (B). DN LINE –DA20,DB20
10. TRACK SECTIONS AT MOO STATION
    - (A). EVALUATOR OF 43–TS, 8–TS, 3161–TS, 3162–TS AT 'MOO' STATION.
11. ALL AUTOMATIC SIGNALS ARE LOCATED CLEAR OF NEUTRAL SECTION(PTFE TYPE).
12. THIS DRAWING SERVES AS STATION SIP AND BLOCK SECTION IS ONLY INDICATIVE, REFER TO ADJACENT BLOCK SECTION SIPs FOR DETAILS.
